


SIBLEY COUNTY DRAINAGE DEPARTMENT REPAIR REPORT

For Staff Documentation & Contractor Information

JD5SN Repair #17-069

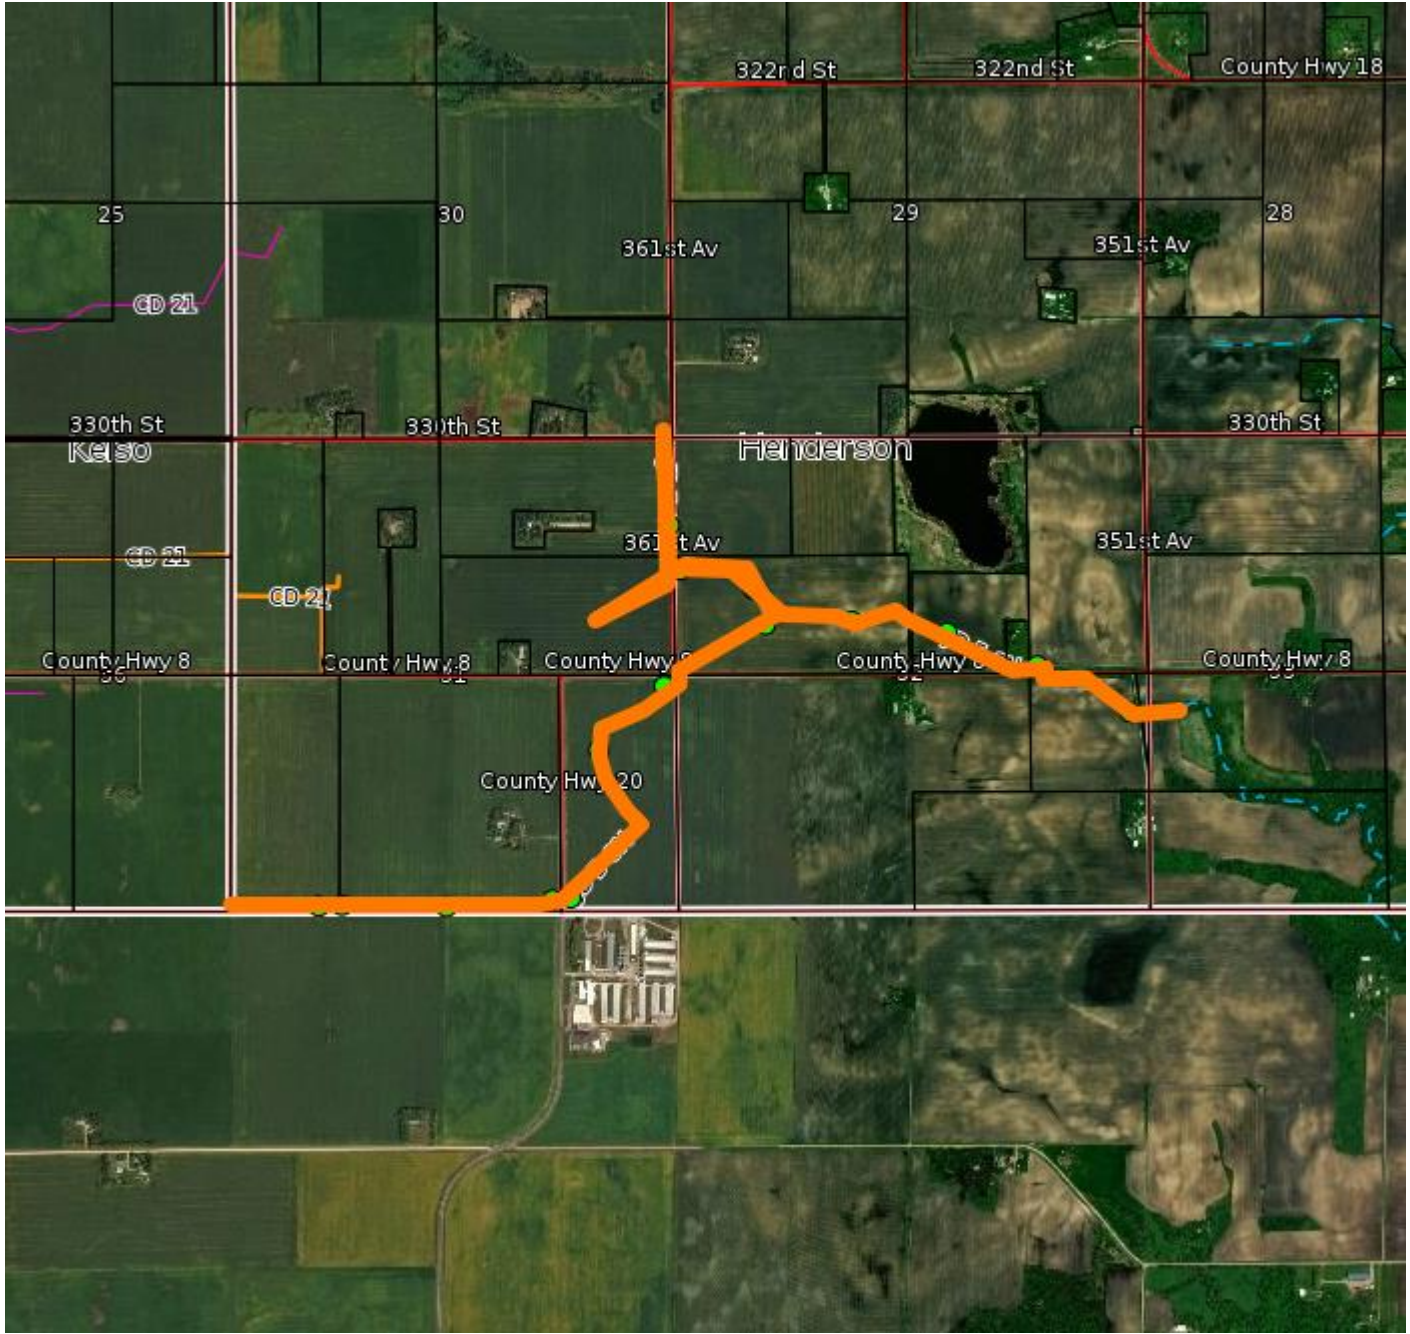

▼ Municipalities 	▼ Public Drainage Systems Open Ditch Shallow Ditch Tile	▼ Drainage System Watersheds
▼ Townships 	▼ Streams Protected Natural Protected Altered Other Perennial/Intermittent	▼ Roads Interstate U.S. and State Hwy CSAH County Road Township Road City Street
▼ Sections 	▼ Private Drainage Drainage Outlet Open Ditch	
▼ County Boundary 		
▼ Parcels 		

SIBLEY COUNTY DRAINAGE DEPARTMENT REPAIR REPORT

For Staff Documentation & Contractor Information

OVERVIEW

Date Repair Was Created:	2017-10-24	Branch:	Entire System
Problem/Proposed Work:	Conduct remote televised reconnaissance of entire county tile line in order to identify critical failures in the system.		
Ditch Repair:			
Tile Repair:			
FEMA Event:	False	FEMA Date:	

REPAIR LOCATION DETAILS

Commissioner District:	1	Township:	Henderson
Twp:	112N	Range:	26W
Section:	33	Qtr-Qtr Section:	
Latitude:	44.464202	Longitude:	-93.988831
Parcel Number:	16.3306.000		
Location Details:			

PERSON REQUESTING REPAIR

Name	Address	Phone
Tim Becker		507-237-4092

LANDOWNER

Name	Address	Phone
LUCILLE A KAHLE	34761 336 ST LE SUEUR MN 56058	

STATUS LOG

Action	Date	Initials	Notes
In Progress	03/02/2018	jennier@co.sibley.mn.us	Paid Empire Pipe for televising invoice #2388, March 16, 2018 claims batch
For Review	05/01/2018	gregd@co.sibley.mn.us	GPS insert spots on tile line with Jesse, found two broken tile, several excavated sites settled, work order to Shannon to fix tile and fill settled areas.
For Review	05/07/2018	gregd@co.sibley.mn.us	Shannon call today 5/7/18, project will take more than \$1500 estimate, connecting issues with tile lines/broken tile. Told him to proceed, \$3000.00 + to repair
Closed	05/23/2018	AaronG@co.sibley.mn.us	Received invoice from SK. Inspected. Repairs complete.
In Progress	12/12/2017	Marileep@co.sibley.mn.us	Ryan from Empire called. They are on the section that is running to the west from Hwy 20. Having to dig a hole every 100' because of what was originally done - tile is coming into the pipes and they were jammed in too far that camera cannot get past. The line itself is in decent shape though. Told them to abandon this portion and move on to the next (Branch 1B)
In Progress	12/13/2017	Marileep@co.sibley.mn.us	Ryan from Empire called. On branch 1, they can only

SIBLEY COUNTY DRAINAGE DEPARTMENT REPAIR REPORT

For Staff Documentation & Contractor Information

			make it 50' because the lines coming in are shoved all the way into the pipe that they are meeting the other side. I told them to abandon this branch for cost purposes and move on.
For Review	10/24/2017	AaronG@co.sibley.mn.us	
In Progress	10/24/2017	AaronG@co.sibley.mn.us	Technician Greg DeVries is working with Empire Pipe Services to arrange televised reconnaissance of the system. Ditch Inspector has sent the contractor maps of the operating area and system to be reconnoitered.
For Review	11/27/2017	gregd@co.sibley.mn.us	
For Review	11/27/2017	gregd@co.sibley.mn.us	revised work order 11/27/17 Greg
In Progress	12/22/2017	Marileep@co.sibley.mn.us	Talked with Dave Evans. Auditor's Office will host a landowner meeting in January or February to decide how to proceed. Perhaps we need to have redetermination on the ditch first?
In Progress	06/13/2018	AaronG@co.sibley.mn.us	Review of meeting notes indicates the following actions need to be taken: 1) Follow up with Justin Black on SEH inspection. 2) Hire contractor to televise beneath road. 3) Inspect the outlet. 4) GPS televising access points (done). 5) Review with David Schauer. 6) Update landowners.
In Progress	06/13/2018	AaronG@co.sibley.mn.us	Spoke with Justin Black. Sent original project plans and meeting notes to him. He will investigate project history available from SEH.

DRAINAGE AUTHORITY ACTIONS

Action	Date	Board Date	Initials	Notes
For Approval	11/14/2017	2018-02-06	jennier@co.sibley.mn.us	approved at 11/14/17 mtg

REPAIR ESTIMATES

Order	Date	Contractor	Total Cost	Notes
1	2017-10-31	EMPIRE PIPE SERVICES	11639.61	Estimate/Work Order for televised recon of JD5.
2	2017-11-27	SK TRUCKING AND EXCAVATING	4500.00	Work at the direction of Empire Pipe services, could be 4-5 days opening areas to pipe as needed to televise County tile line, send bill to Sibley County.
3	2018-05-01	SK TRUCKING AND EXCAVATING	1500.00	Fill in settled excavated areas as needed North of County Road 8, and West of County road 21, also dig open and repair as needed two flagged spots for broken county tile, County will pay labor and material, finish by 6/1/18
